


FROM THE BUILDER

- Lots 48-53 (units 9-14) prepping for paint, tile work and temp power
- Lots 42-47 (units 15-20) painting, installing fixtures
- Lots 40-41 (units 21-22) drywall finished, cabinets being installed
- Lots 37-39 (units 23-25) drywall finished
- Lots 35-36 (units 26-27) drywall hung
- Lots 33-34 (units 28-29) insulation complete, waiting on drywall, siding is almost complete
- Lots 28-32 (units 30-34) decks built, rough-ins started
- Lots 24-27 (units 35-38) framing punch, stairs installed
- Lots 20-23 (units 39-42) framing started
- Lots 33-41 (units 21-29) Lateral water and sewer tie ins completed
- Site work for drives started

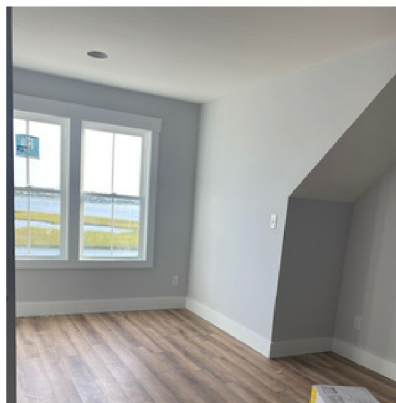

Be on the lookout for another update in two weeks!
